
SE _LAB2

NAME : JAYASHREE D

SRN : PES2UG24CS203

SECTION : D

1. Creating epic

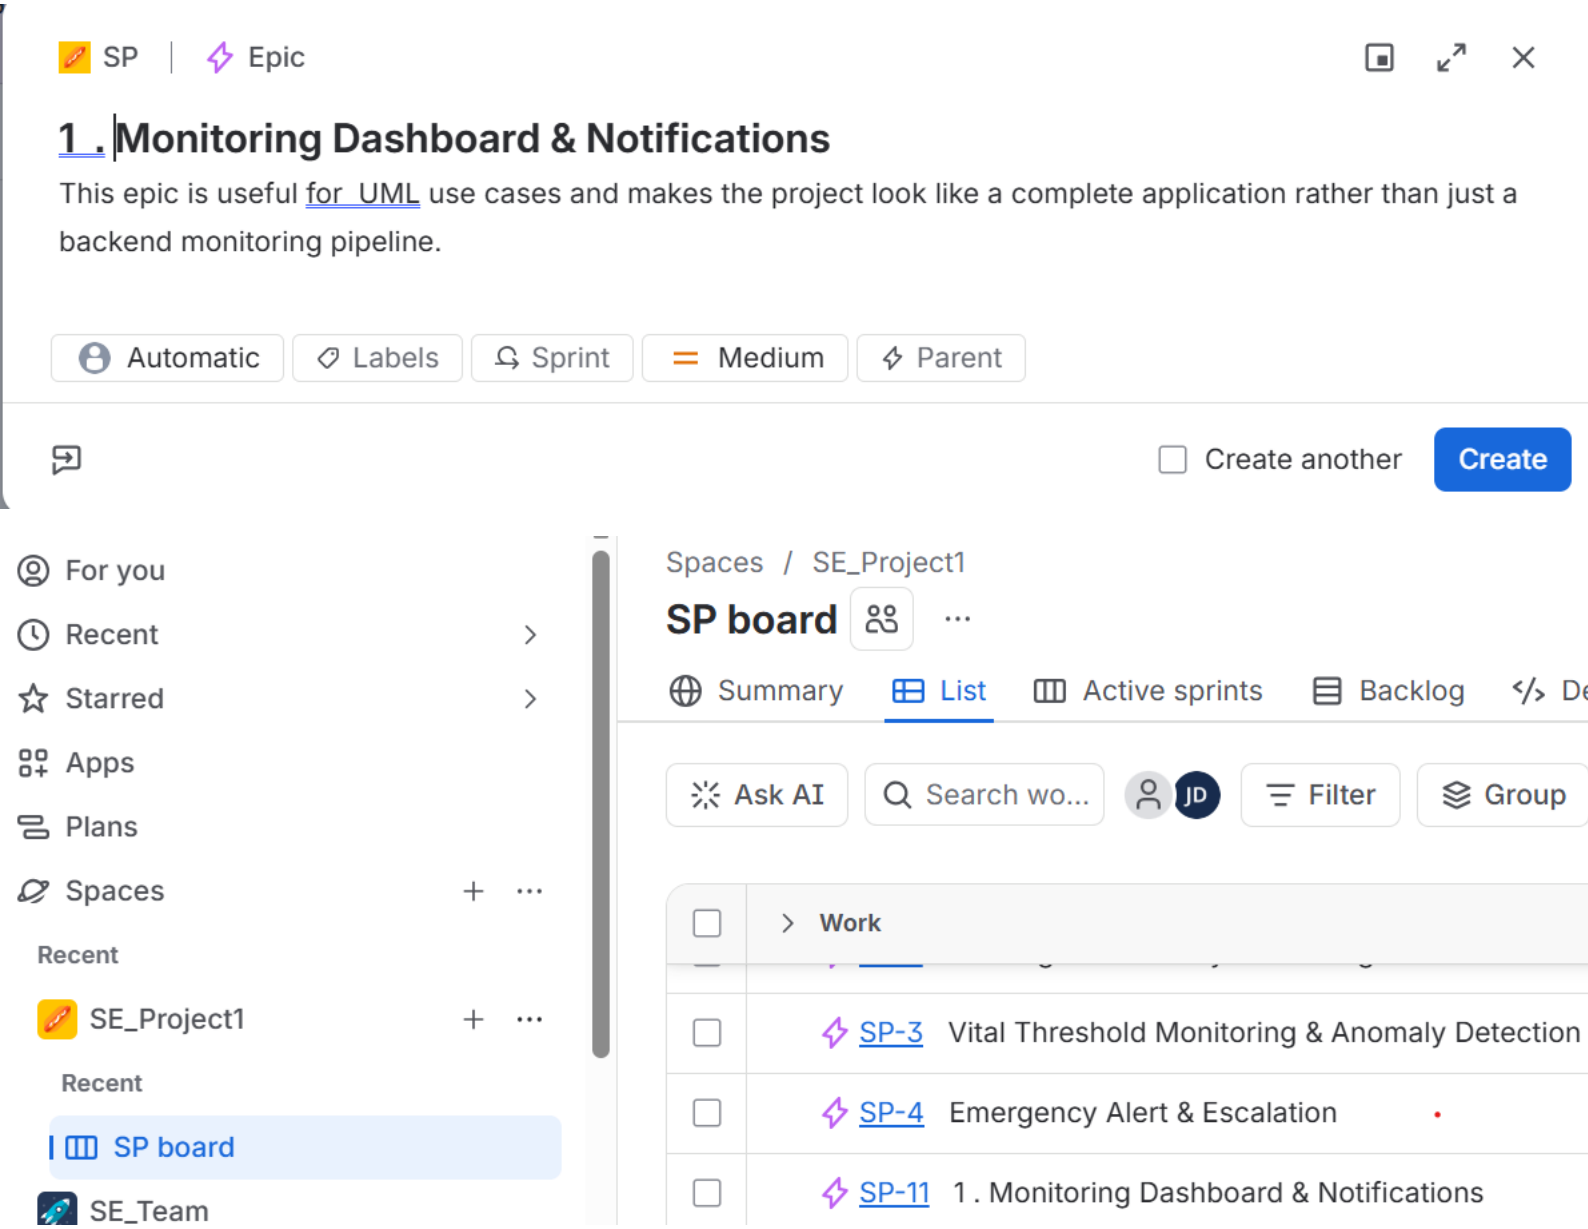

2. Adding user story to the above epic

SP | Story

View Current Vitals

> As a caregiver, I want to view a patient's current SpO_2, heart rate and blood pressure so that I can monitor the patient's condition.

Automatic | SP-11 | Sprint | Medium | Labels

Create another | Create

Spaces / SE_Project1


SP board


Summary | List | Active sprints | Backlog | Development | Forms | Timeline | Docs | Reports

Ask AI | Search work | Filter | Group

Work	Assignee	Reporter	Priority	Status
SP-1 Patient & Caregiver Management	Unassigned	Jayashree D	Medium	To Do
SP-2 Vital Signs Telemetry & Data Ingestion	Unassigned	Jayashree D	Medium	To Do
SP-3 Vital Threshold Monitoring & Anomaly Detection	Unassigned	Jayashree D	Medium	To Do
SP-4 Emergency Alert & Escalation	Unassigned	Jayashree D	Medium	To Do
SP-11 1 . Monitoring Dashboard & Notifications	Unassigned	Jayashree D	Medium	To Do

3. Creating Sprint for a user story

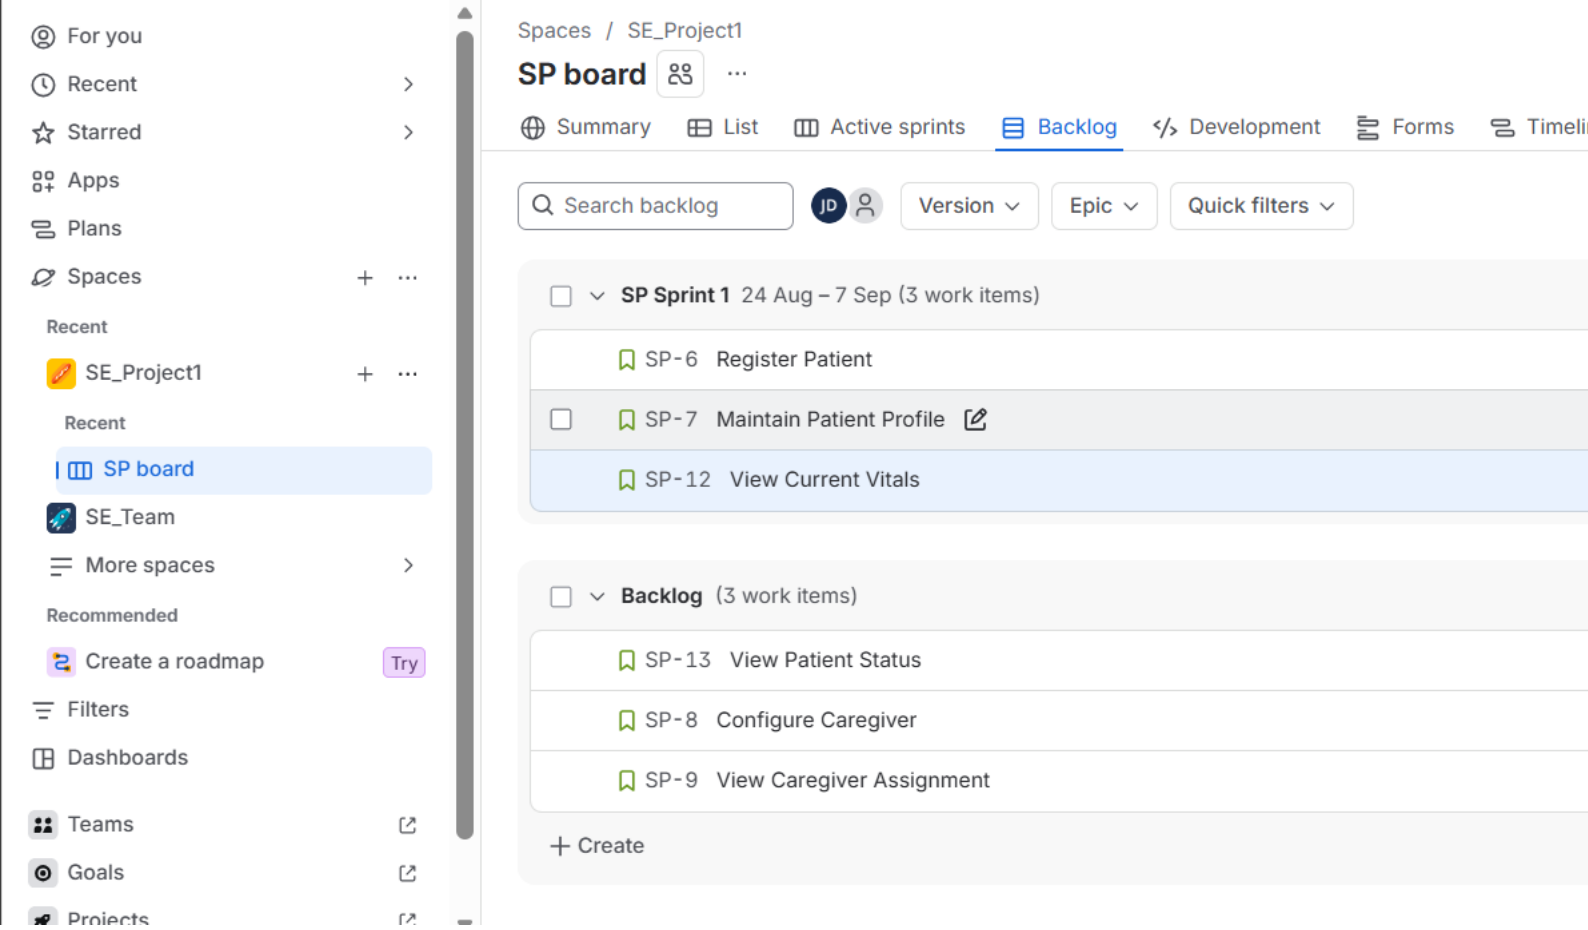

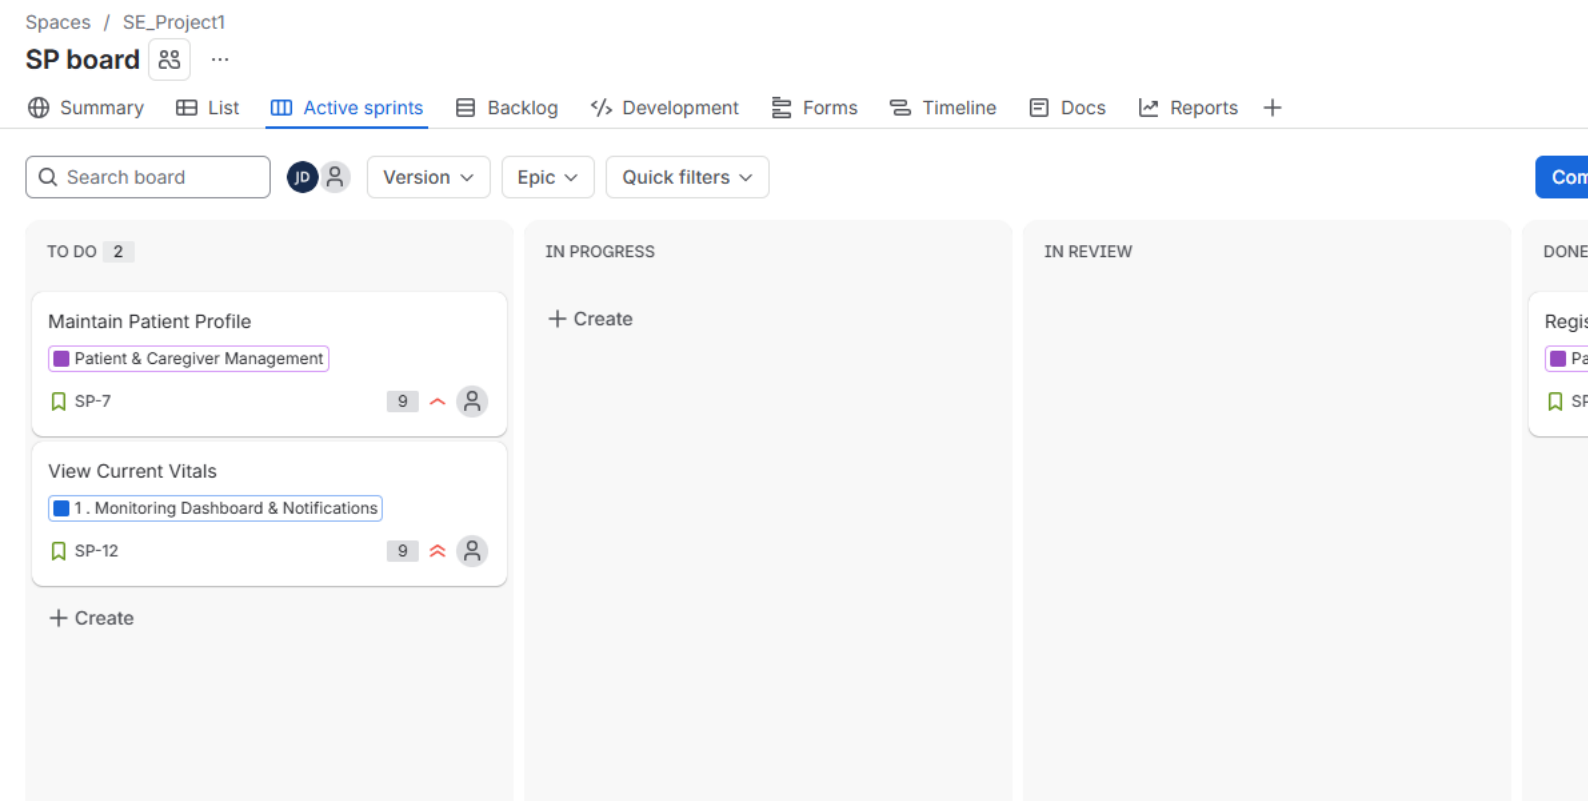

4. Assigning Priority and Story Points
   (Jira Backlog with Epics and User Story)

Spaces / SE_Project1

SP board

Summary | List | Active sprints | Backlog | Development | Forms | Timeline | Docs | Reports

Search backlog | Version | Epic | Quick filters

SP Sprint 1 24 Aug – 7 Sep (3 work items)

- SP-6 Register Patient
- SP-7 Maintain Patient Profile
- SP-12 View Current Vitals

Backlog (10 work items)


- SP-8 Configure Caregiver
- SP-19 Maintain High Availability
- SP-20 Secure Patient Data
- SP-21 Performance Testing
- SP-22 Security Testing
- SP-23 US-4.1 — Generate Emergency Alert
- SP-24 US-4.2 — Notify On-Call Caregiver
- SP-25 US-4.3 — Escalate Unacknowledged Alert
- SP-26 US-4.4 — Acknowledge Alert
- SP-27 US-4.5 — Record Alert History

+ Create

5. Burndown Chart

Spaces / SE_Project1 / SP board / Reports

Burndown Chart

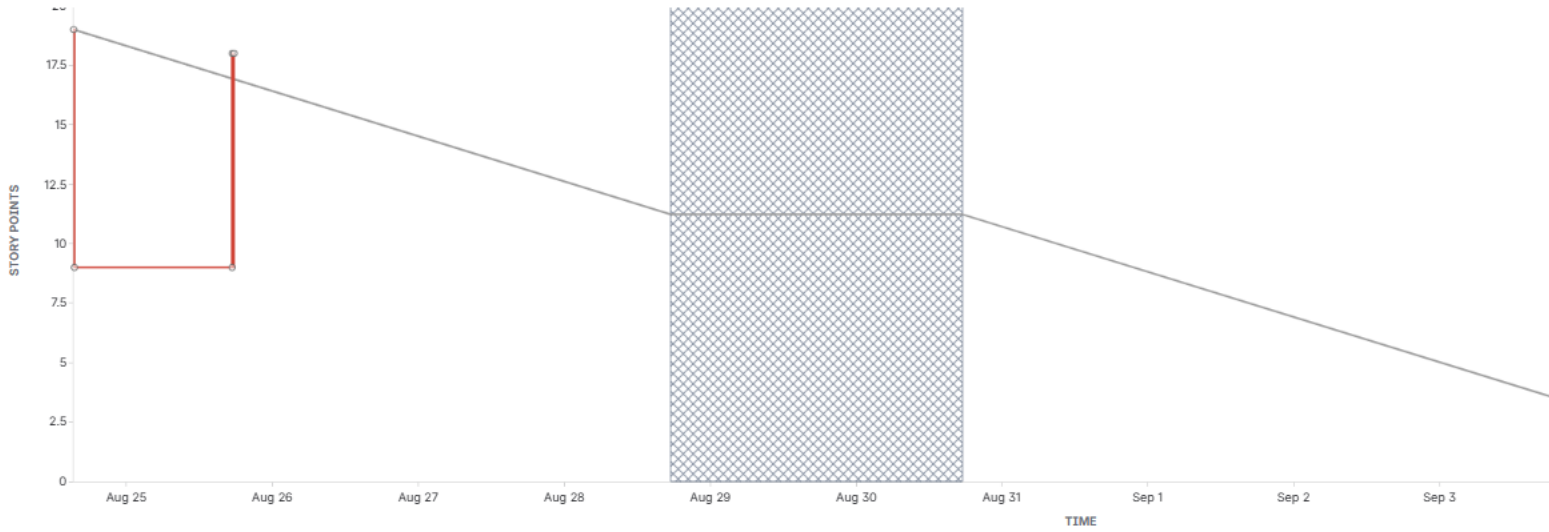

Date	Issue	Event Type	Event Detail
24/Aug/26 3:18 PM	SP-6	Sprint start	
	SP-7		
	Total		
24/Aug/26 3:25 PM	SP-6	Burndown	Issue completed
25/Aug/26 5:21 PM	SP-12	Scope change	Issue added to sprint
	SP-7	Burndown	Issue completed
25/Aug/26 5:40 PM	SP-7	Burndown	Issue reopened

Reflection Questions:

1. Did your estimations reflect the actual effort?

My estimations were reasonably close to the actual effort for the user stories that were implemented in the backlog. However, some tasks took more effort than initially expected, especially those related to emergency alerts, monitoring, and security/performance requirements. Since user stories were added mainly under Epics SP-1, SP-4, SP-11 , SP-17, the effort estimation was more accurate for these areas, while Epics SP-2 and SP-3 were not explored in the same level of detail. Overall, the sprint helped us understand that better task breakdown is necessary for more accurate estimation.

2. Was your backlog well-prioritized?

Yes, the backlog was prioritized around the important features of the healthcare monitoring system. We focused on patient and caregiver management, emergency alert and escalation, monitoring/notifications, and security, performance and reliability. These were placed ahead of less-developed areas because they are important for making the system usable and safe. However, the backlog could be improved by adding and prioritizing user stories for vital-sign data ingestion and threshold/anomaly detection, which are also core parts of the problem statement.

3. How did your simulated sprint align with your plan?

The simulated sprint generally aligned with our plan because we focused on the epics where we had already created user stories—Patient & Caregiver Management, Emergency Alert & Escalation, Monitoring Dashboard & Notifications, and Security, Performance & Reliability. The sprint helped us organize the work into smaller deliverables and understand how the different features contribute to the overall monitoring application. However, since Epics SP-2 and SP-3 did not yet have user stories, those areas remained outside the main sprint workload and would need to be addressed in a future sprint.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart helped us understand how much work the team was able to complete during the simulated sprint and whether the remaining work was decreasing as planned. It showed that our capacity was influenced by how well the work was broken down into user stories and tasks. It also highlighted that having fewer stories under some epics can make the sprint workload appear smaller than the actual scope of the project. From this, we learned that future sprints should include properly defined stories across all major epics so that the team's actual workload and capacity can be measured more accurately.
